



Bond Oversight Committee Meeting January 21, 2015

North Monterey County Unified School District

Current Bond Projects

- Deferred Maintenance
- Technology Upgrades
- Library Media Center
- HS Gym Floor/Bleacher
- Athletic Track & Field
- HS HVAC Upgrades
- Centralized Operating Costs
- Total

- \$.5M
- \$.75M
- \$3M
- $\sqrt{\$}.5M$
- \$ 5M
- \$ 5.5M
- \$.25M

\$15.5M

Deferred Maintenance 2014

Castroville	\$24,340
-------------------------------	----------

- Echo Valley \$20,008
- Elkhorn \$20,678
- Prunedale \$12,832
- NMC Middle School \$17,580
- NMC High School \$27,544
- Central Bay
- Total Expenditures \$122,982

Deferred Maintenance

Deferred Maintenance Projects

- Classroom Upgrades for Technology Infrastructure
- Flooring Covering Replacement
- Painting Projects (Interior & Exterior)
- Building Repairs (Gutters, Minor Roofing, Ramps, Etc.)
- Fire Alarm Panel Replacement
- Drinking Fountain Replacement
- Parking Area-Asphalt Patch & Striping
- Domestic Water & Irrigation Pump Controllers

Many of the items listed above are noted on the Williams List and are essential projects that need to be completed.



Technology 2014

	Ctro	771	
	$\mathbf{S} \mathbf{I} \mathbf{I} \mathbf{U}$	OV1	16
			10

- Echo Valley
- Elkhorn
- Prunedale
- NMC Middle School
- NMC High School
- Central Bay
- Total Expenditures

- \$66,322
- \$75,010
- \$51,977
- \$5,570
- \$175,293
- \$4,752
- \$398,405

Technology Projects

Technology Improvements

- New Computer Labs
 - Computer Tables and Student Chairs
 - Fiber Connections
 - New IDF Locations for Improved Computer Performance
- New Voice Over Internet Protocol (VOIP)
 - New Telephones (VOIP Compatible)
 - New Networking Equipment (Switches, Cabling, Ethernet Ports)
 - Wireless Access Points (WAPs)
- New White Boards to Compliment Existing Smart Projectors

New Computer Lab



Library / Media Center

Current Project Estimate	\$3,000,000
Construction Other Fees (design, architectural, engineering) Other Related Fees (permits, DSA, surveys, inspection) 10 %Project Design & 10 %Construction Contingency	\$2,000,000 \$300,000 \$315,000 \$385,000

Mandatory Upgrades Include the Following:

- Restroom Renovation
- Fire Alarm Upgrade
- Elevator Access / Stair Modification
- Accessible Casework (checkout desk)
- Door Hardware Replacement
- Path Of Travel (POT) Site work


Optional Upgrades Include the Following:

- Career Center at Mezzanine
- Staff Development Center (lower level)
- Family Resource Center (computer lab)
- Lighting & HVAC Upgrade
- Architectural Appearance (new finishes)

Library/Media Center Sample Timeline for Project

- Step 1: Schematic Design (Estimated 10 to 12 weeks)
- Step 2: Stakeholder Consult (2 days)
- Step 3: Submit to DSA for Review (3 months)
- Step 4: Resubmit for DSA backcheck (1 month)
- Step 5: Prepare & advertise for bids (30 days)
- Step 6: Board Review and Approval; Issue Notice of Award (2 to 4 weeks)
- Step 7: Bid Awardee Response time (10 days)
- Step 8: Construction Begins! (8 months)
- Step 9: DSA Closeout Now REQUIRED!
- Step 10: Occupy Building

Library Media Center

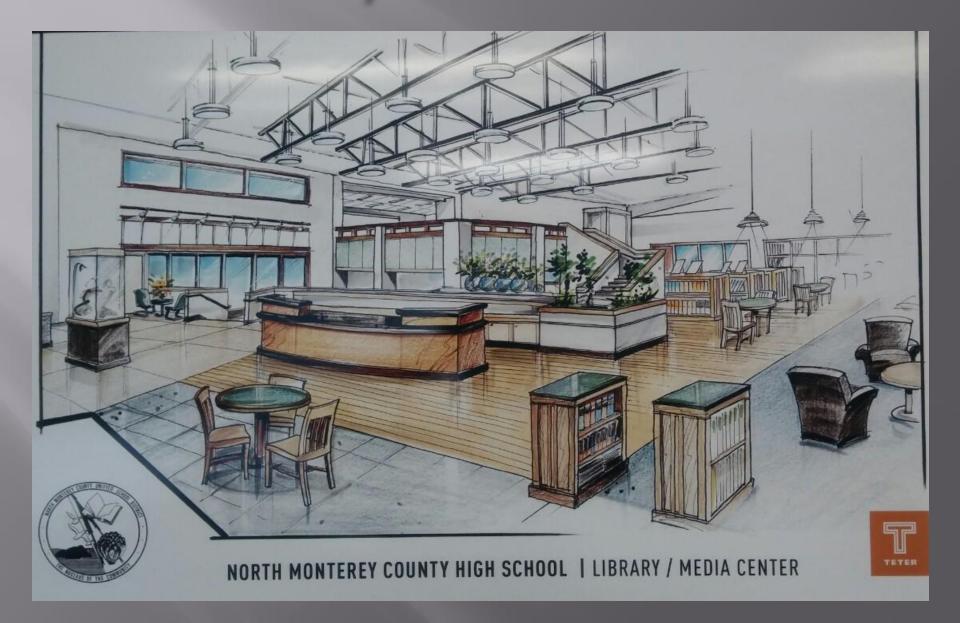

NMCHS Gym Bleachers Flooring Replacement

Project Includes Replacing Bleachers and Floor Covering

Current Project Estimate	\$500,000
Construction	\$315,000
Other Fees (design, architectural, engineering)	\$60,000
Other Related Fees (permits, DSA, testing, inspection)	\$45,000
10 %Project Design & 10 %Construction Contingency	\$60,000
Additional Cost for HazMat Disposal	\$20,000
Total Expenditures thru 12/31/2014	\$1,526

Athletic Track & Field

Current Project Estimate	\$5,100,000
Construction Other Fees (design, architectural, engineering) Other Related Fees (permits, SWPP, surveys, bonding) Project Design & Construction Contingency	\$3,400,000 \$300,000 \$300,000 \$500,000
Estimate Includes the Following: All Weather Track Synthetic Turf Field Demolition Grading Trainage / Utilities Hardscape (Asphalt, Concrete, Retaining Wall) Site Furnishings (Press Box, Goal Posts, Etc.) Soft scape (Shrubs, Trees, Ground Cover) Irrigation and Electrical Allowances Exterior Lighting	
■ Plus restroom/concession building replacement	\$500,000
Total Expenditures thru 12/31/2014	\$18,339

Athletic Track & Field



NMC High School HVAC

Current Project Estimate

Undetermined

- HVAC Systems assessment
- Determine scope of work for project
- Establish budget for project
- Board approval to proceed

Bond Project Expenditures Summary

\$122,982

\$398,405

Bond Project Expenditures To Date

E Deferred Maintenance	•	Deferred	Maintenance
------------------------	---	----------	-------------

- Technology Upgrades
- Project Planning\$ 19,865
- Total \$541,252
